



ATHLETICS CANADA

ROAD RACE MEASUREMENT CERTIFICATE

Race Information

Name of the course _____
Certificate number _____ Distance _____ Race date _____
City _____ Province _____
Race contact name _____ Race contact email _____

Course Information

Start elevation _____ Finish elevation _____
Elevation change _____ Percent separation _____

Measurer Information

Measurer name _____
Measurement date _____ Expiry date _____

Official Notice

Based on examination of data provided by the above named measurer, the course described above and in the map attached is hereby certified as reasonably accurate in measurement according to the standards adopted by the **Road Running Technical Council**. If any changes are made to the course, this certification becomes void, and the course must then be recertified.

Validation of Course

In the event a **National Open Record** is set on this course, or at the discretion of **Athletics Canada**, a validation remeasurement may be required to be performed by a qualified measurer. If such a remeasurement shows the course to be short, then all pending records will be rejected and the course certification will be cancelled.

As Nationally Certified by


Signature of certifier _____ Date _____

Any inquiries regarding this certificate should be directed to coursemeasurement@athletics.ca





NOT TO SCALE

2022 Canadian Half Marathon Championships Winnipeg, Manitoba

Hosted by




MANITOBA Marathon



Athletics Canada Certified
MN-2022-027-BDC
Certification Expires Dec 31/2026

Measured June 7 and 8, 2022 by
Laurent Lacroix - WA/AIMS Grade A
Jeff Munday

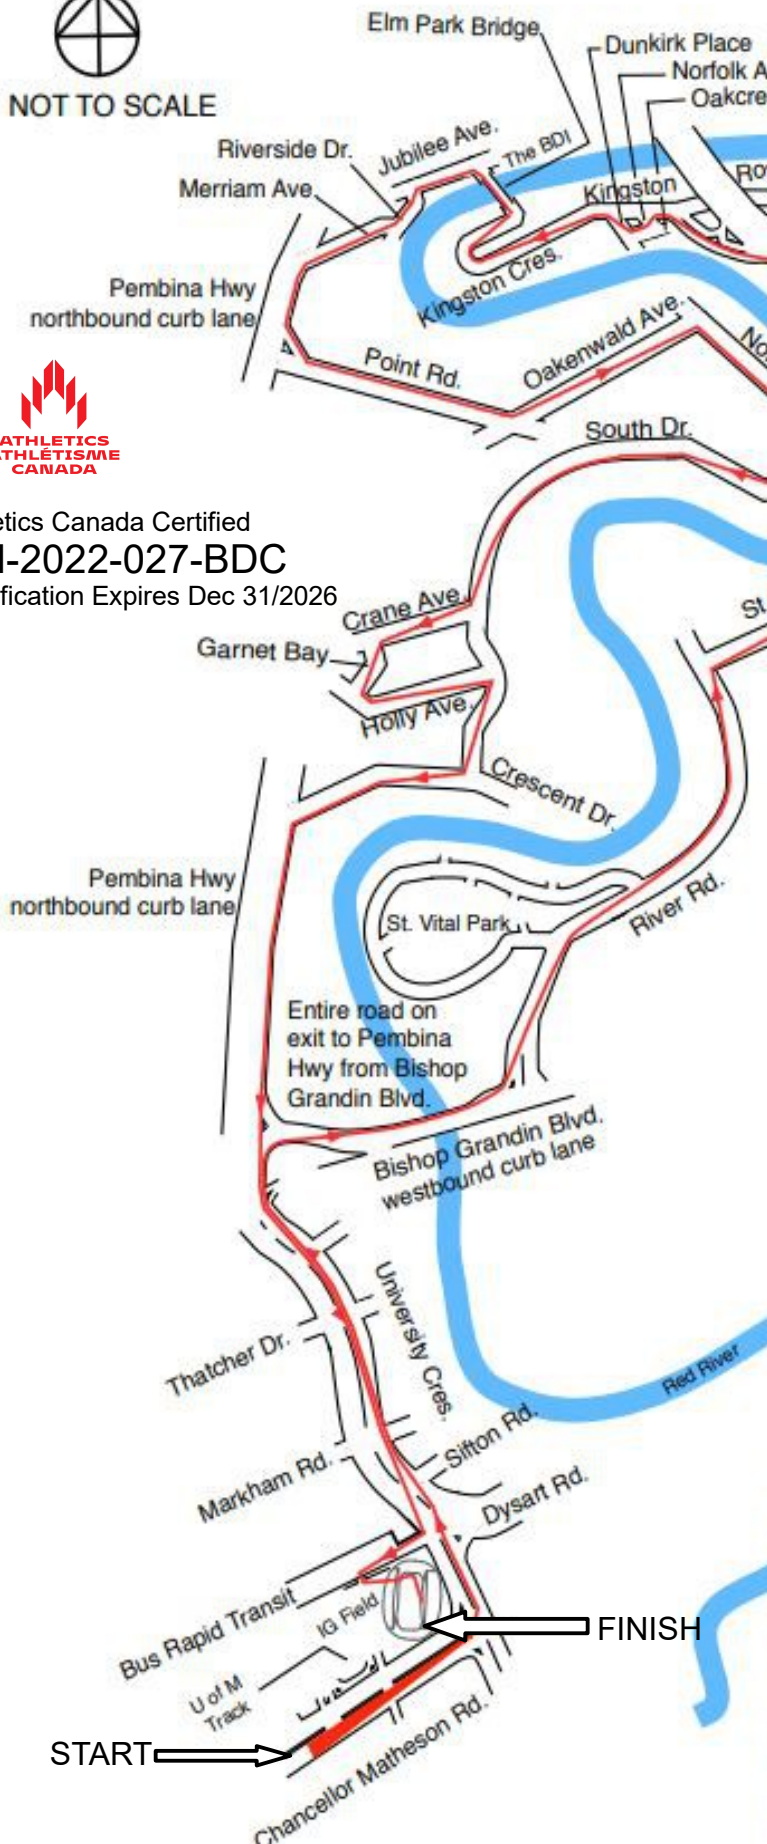

Finish Line
Center field stripe at the 55 yard line line with east edge of the Jumbotron screen on the north side of the field.

- a. 24.515 m from the wall below the south edge of electrical outlet NE1A-6.
- b. 23.440 m from the wall along the center field stripe.
- c. 25.095 m from the wall below the south edge of electrical outlet SE1A-9

IG Field Steel Tape Measurement

- d. Finish line to north goal post: 55.47 m
- e. North goal post to west edge of metal grate by cement wall: 38.05 m
- f. West edge of metal grate by cement wall to loading dock door: 39.66 m
- g. loading dock door to concrete nail in seam: 13.076 m

Total distance: 146.225 m

Nail in concrete seam to north-south groove in lamp post base outside IG Field gate: 128.329 m

274.554 m from lamp post outside gate to the finish line.

Start line, facing North

Start line, facing SSW

START

FINISH
